


# MIDDLE RILEY CREEK REVISED SCHEDULE

ID	Task Name	Duration	Start	Finish	'21							Oct 31, '21					
					M	T	W	T	F	S	S	M	T	W	T	F	
1	<b>Middle Riley Creek</b>	<b>7 days</b>	<b>Wed 10/27/21</b>	<b>Thu 11/4/21</b>													
2	<b>South Phase</b>	<b>7 days</b>	<b>Wed 10/27/21</b>	<b>Thu 11/4/21</b>													
3	Boulder Wall	3 days	Wed 10/27/21	Fri 10/29/21													
4	Storm Sewer	1 day	Mon 11/1/21	Mon 11/1/21													
5	Finish Grading	1 day	Tue 11/2/21	Tue 11/2/21													
6	Restoration	2 days	Wed 11/3/21	Thu 11/4/21													
7																	
8	<b>North Phase</b>	<b>3.5 days</b>	<b>Thu 10/28/21</b>	<b>Tue 11/2/21</b>													
9	Clear & Grub	0.5 days	Thu 10/28/21	Thu 10/28/21													
10	Creek Realignment	0.5 days	Thu 10/28/21	Thu 10/28/21													
11	Vanes/Riffle	1 day	Fri 10/29/21	Fri 10/29/21													
12	Coir Logs	0.5 days	Mon 11/1/21	Mon 11/1/21													
13	Restoration	1 day	Mon 11/1/21	Tue 11/2/21													

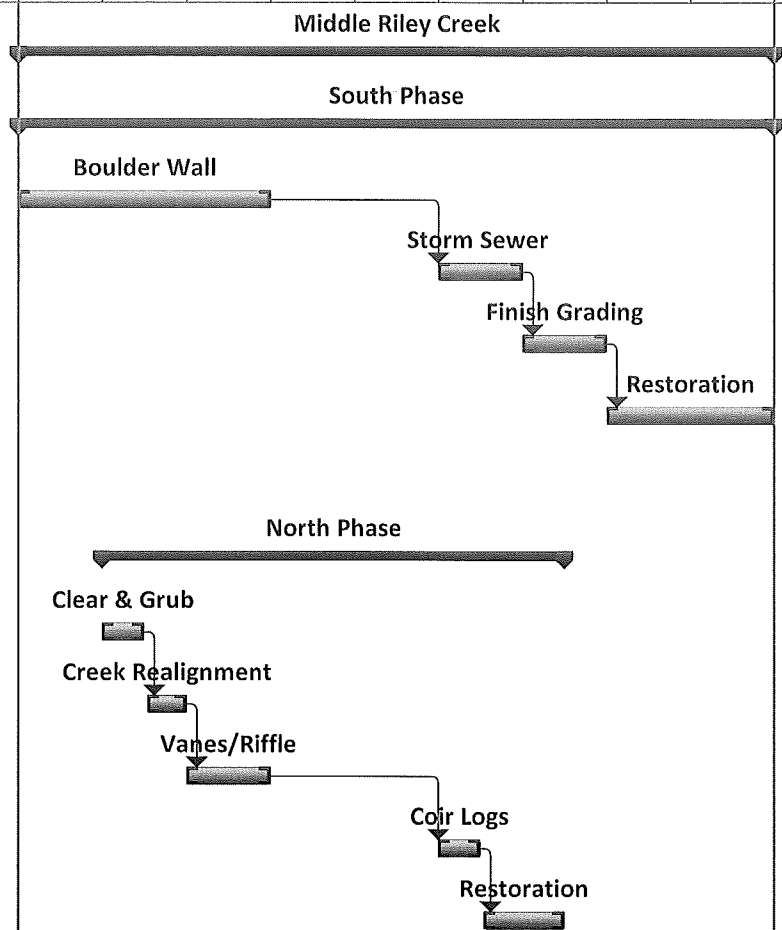

Project: Middle Riley Creek 10-27 Date: Wed 10/27/21	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
